


York Station Gateway

This Presentation includes

- An update on completed works and works taking place
- Upcoming works
- Questions/discussion

Section 7/7A – Piled Wall, Demolition, and Civils

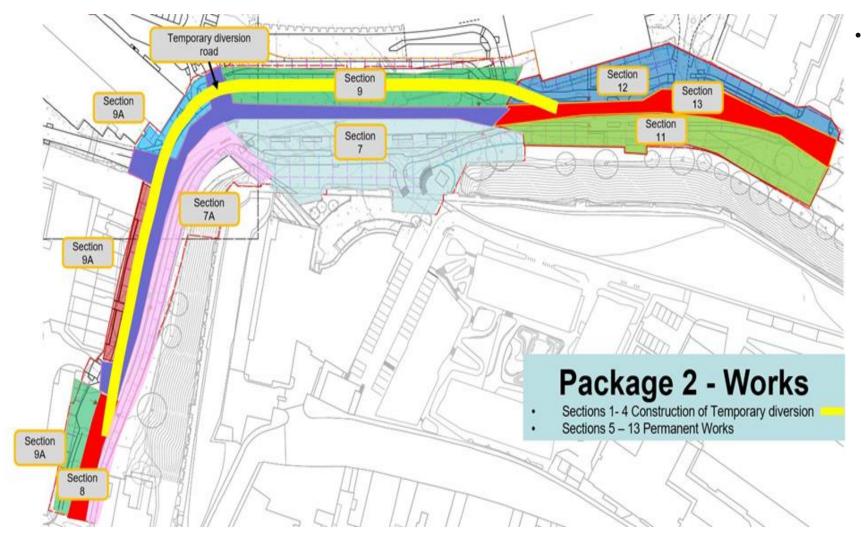

Achievements:

- All piles have been installed, and capping beam is in place
- Remaining structure demolished
- Majority of drainage and groundworks have been completed.
- Work on above-ground features has commenced.





Stone Batter (Topsoil to go over the top)

Capping Beam

Other works that have taken place

- Ducting, tree pits, kerbing and drainage works in section 7
- Dwarf wall in section 7A taken down (and stone set-aside)

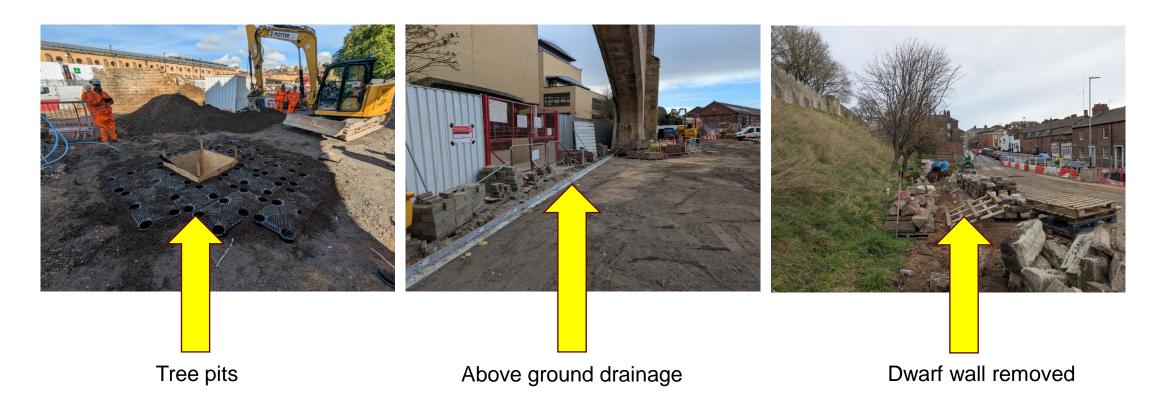

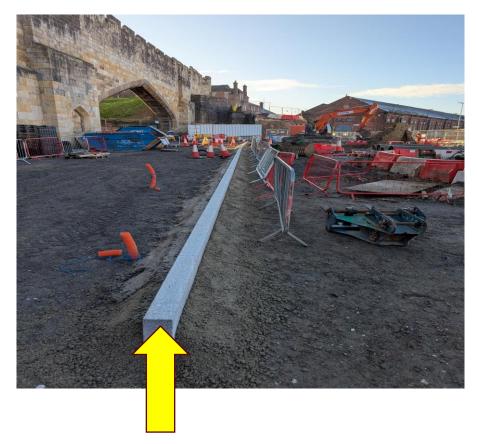

Kerbs installation in progress



Dig down for new bus lay-bys

Upcoming works – Traffic Management / Bus Stops

- 2-way traffic to be maintained at all times
- Once Section 7 is complete, traffic will be redirected to this area, allowing work to commence in Section 11
- New bus stops will be completed before moving into areas with existing bus stops to facilitate their relocation.
- Details around changes to buses and bus routes will be communicated separately by the bus companies

Section 7/7A – Next Steps

Next Steps (up to Christmas):

- Complete gas diversion and decommission the Gas Governor.
- Yorkshire Water to carry out sewer works in mid-December
- Continue with remaining groundworks
- Complete above-ground features, including kerbs and paving.
- Install street furniture such as lighting columns/bus shelters/ticket machines etc.
- Start works on Footway down the side of Delrio's Restaurant in Feb 2025 in Section 7A 5 weeks work utilising a lane closure
- Work will move to the southbound side outside the Portico (Section 11) in March 2025.

Delays:

- 1. Due to design issues
- 2. Unforeseen buried services
- 3. The retention of the Gas Governor (to be fully removed before Christmas)
- 4. Yorkshire Water sewer works (Yorkshire Water commencing works in December)

Questions/Discussion...
