

KEY

PROPOSED LANDSCAPE DELIVERY PHASES

Phase One (2021 / 2022)

Landscape delivery stage 1: ground cultivation, pond creation, path and fence installation, cyclepath installation, paths linking woodland (autumn)
 Landscape delivery stage 2: sow relevant seed mixes (autumn / spring)
 Landscape delivery stage 3: plant all woodland blocks & individual trees & shrubs as indicated on DLD (winter)
(c.36,000 trees in woodland blocks alone)

Phase Two (2022 / 2023)


Landscape delivery stage 1: ground cultivation, pond creation, path and fence installation (autumn)
 Landscape delivery stage 2: sow relevant seed mixes (autumn / spring)
 Landscape delivery stage 3: plant all woodland blocks & individual trees & shrubs as indicated on DLD (winter)
(c.17,500 trees in woodland blocks alone)

Phase Three (2023 / 2024)

Landscape delivery stage 1: ground cultivation, path and fence installation (autumn)
 Landscape delivery stage 2: sow relevant seed mixes (autumn / spring)
 Landscape delivery stage 3: plant all woodland blocks & individual trees & shrubs as indicated on DLD (winter)
(c. 26,300 trees in woodland blocks alone)

Subsequent Phases

Indicative areas for future creation of Forest School; Visitor Centre; Eastern Gateway Entrance; Community Woodland Planting

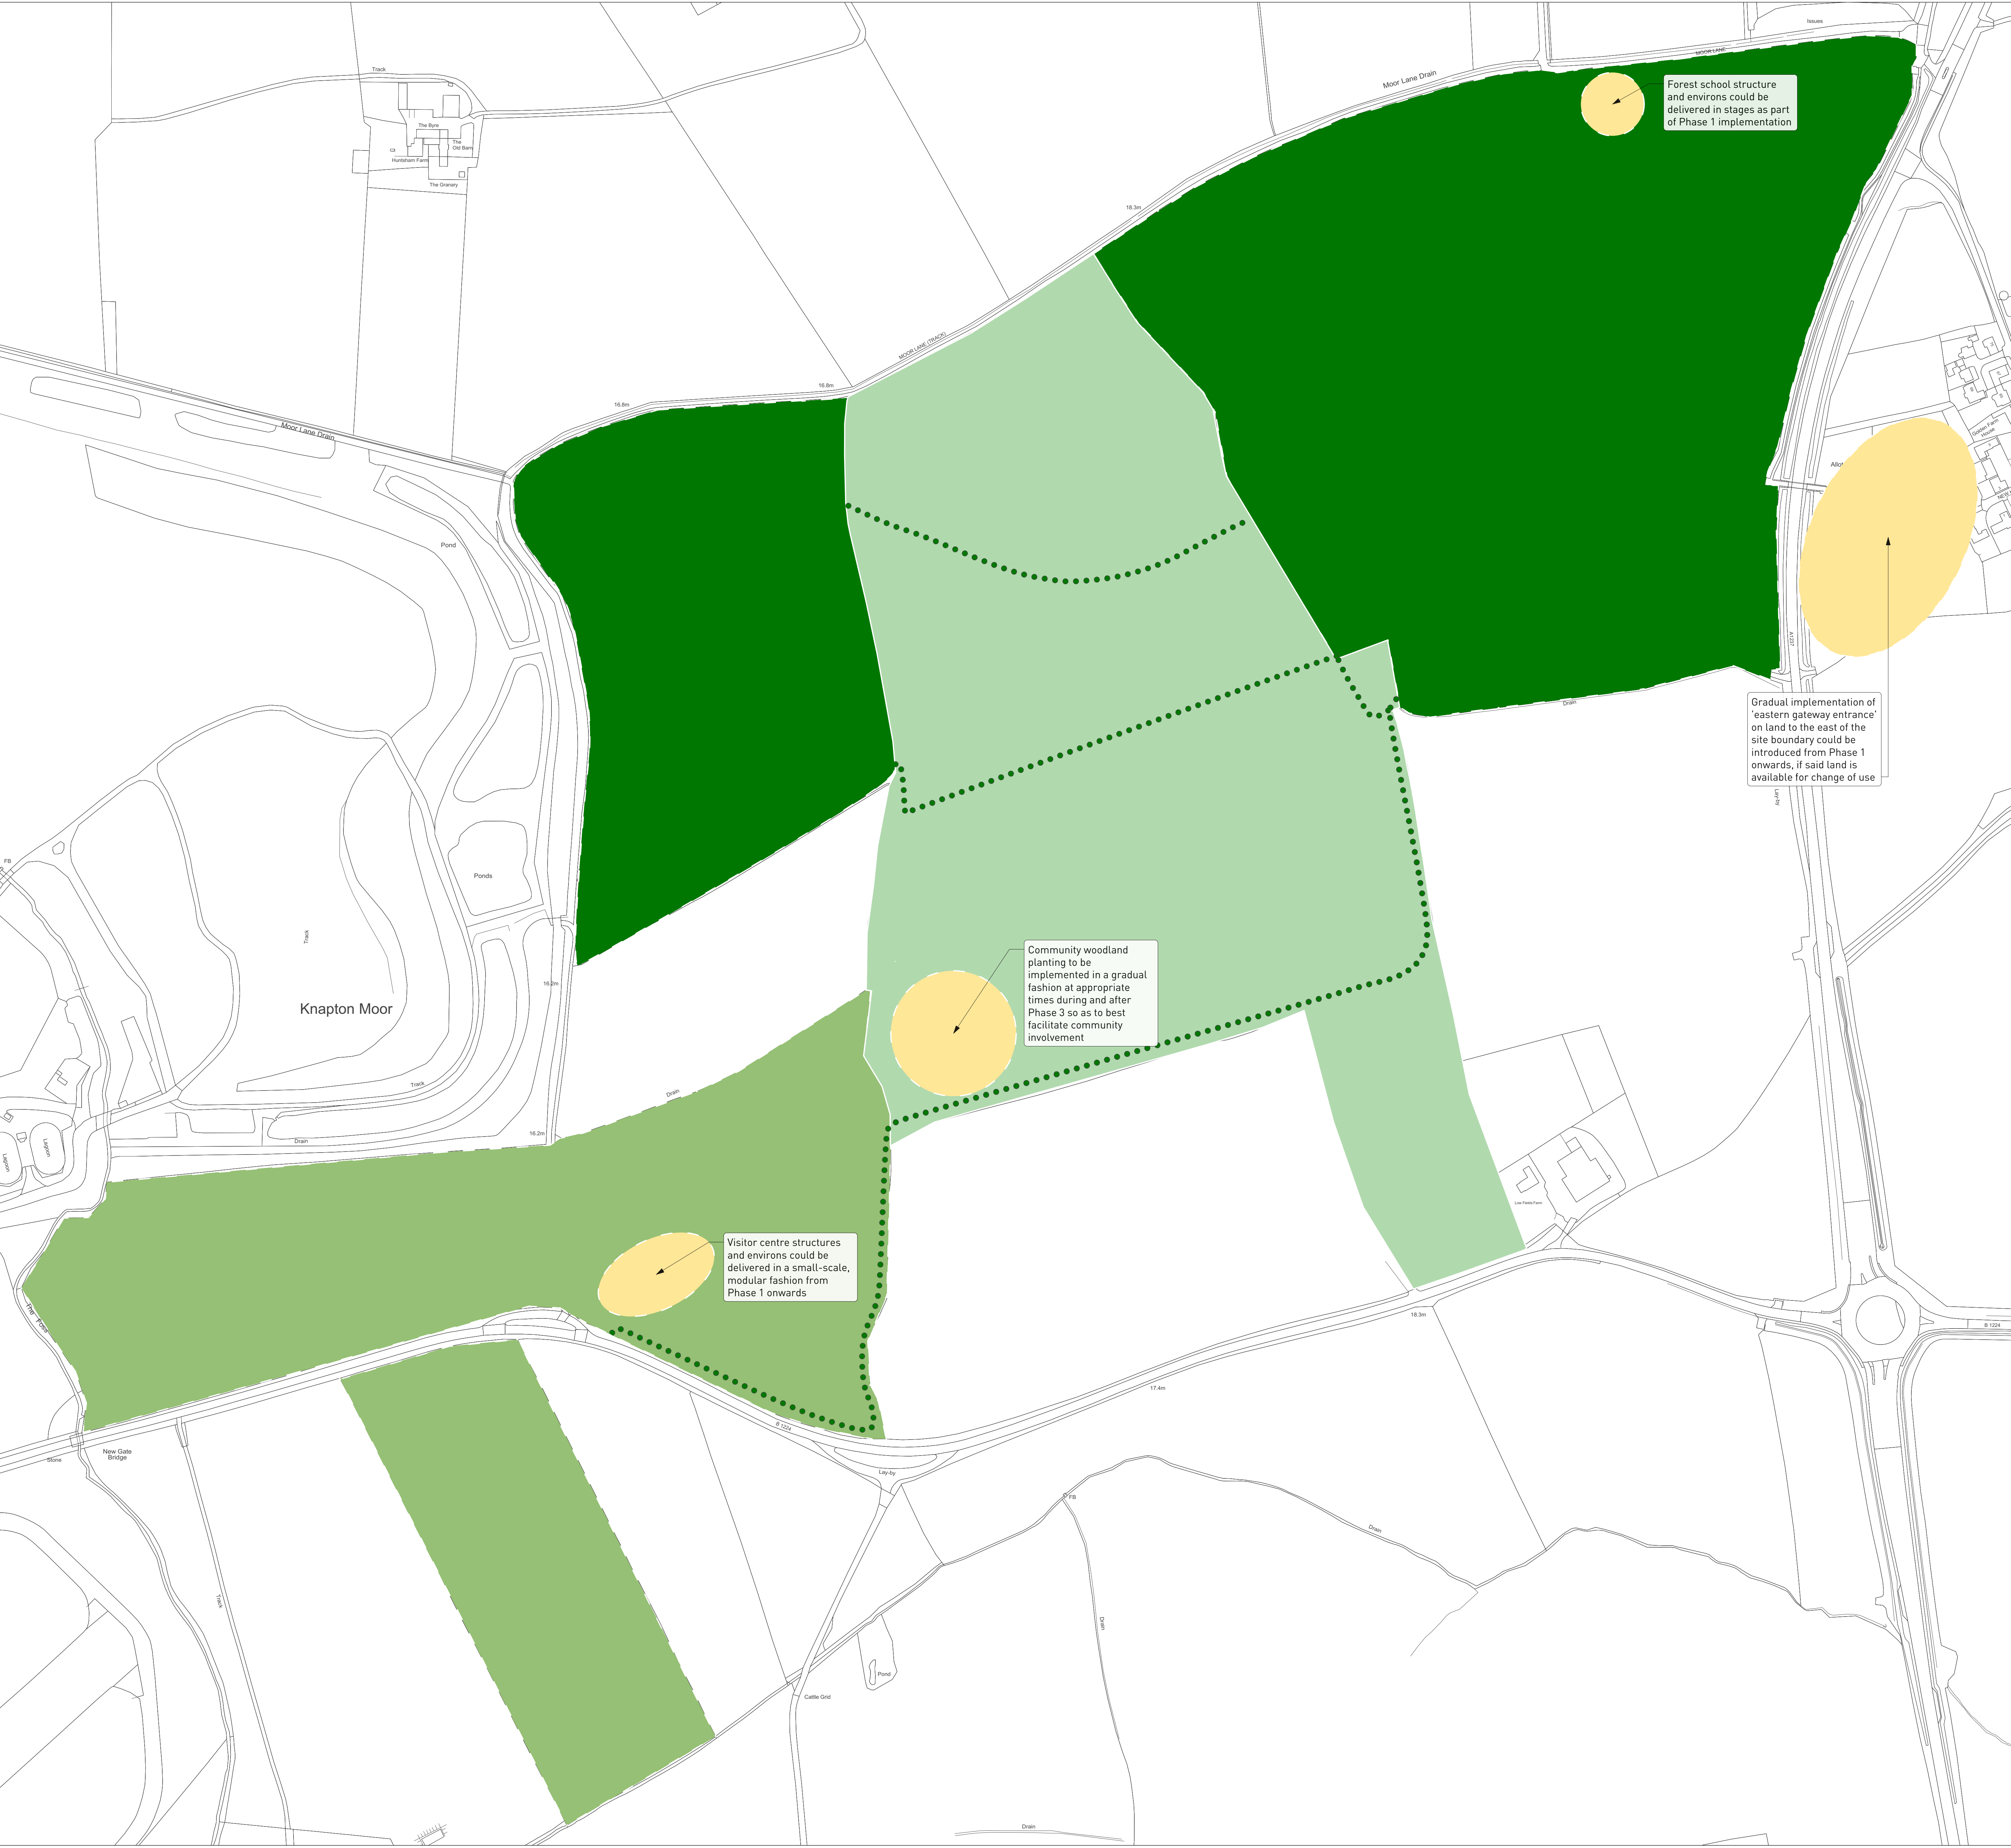

Rev	Date	By	Note
A	16.08.21	VR	Phasing updates

Phasing Plan
 York Community Woodland

Client: City of York Council
 DRWG No: P21-1688.002 REV: A
 Drawn by: VR/KG Approved by: KC
 Date: 06/08/2021
 Scale: 1:2,000 @ A0

