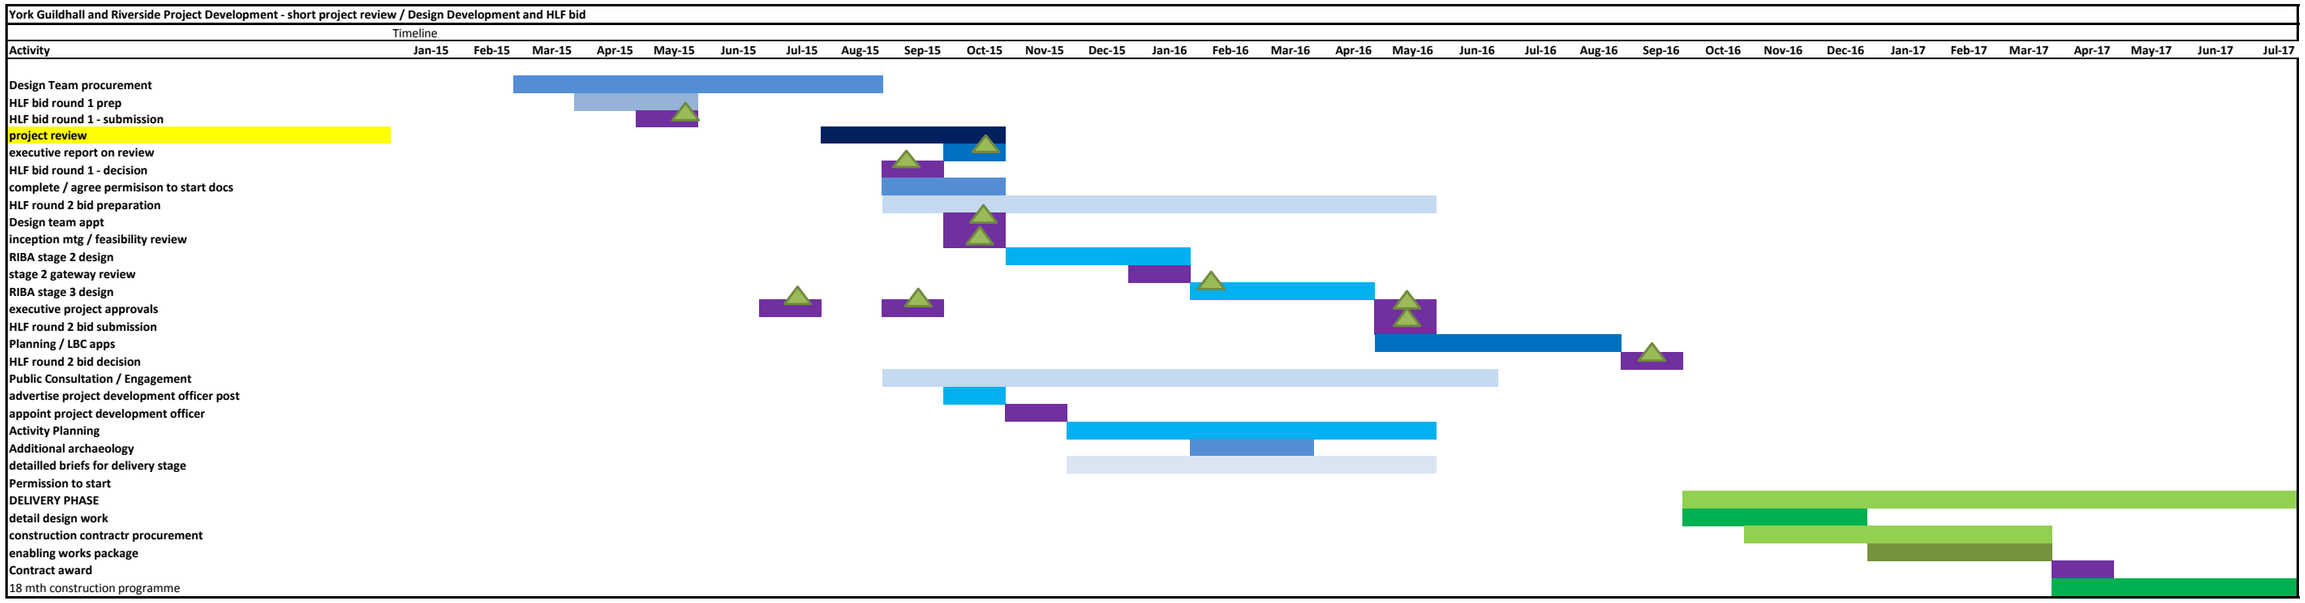
York Guildhall and Riverside Project Development - short project review / Design Development and HLF bid
Timeline
Activity
Jan-15
Feb-15
Mar-15
Apr-15
May-15
Jun-15
Jul-15
Aug-15
Sep-15
Oct-15
Nov-15
Dec-15
Jan-16
Feb-16
Mar-16
Apr-16
May-16
Jun-16
Jul-16
Aug-16
Sep-16
Oct-16
Nov-16
Dec-16
Jan-17
Feb-17
Mar-17
Apr-17
May-17
Jun-17
Jul-17
Design Team procurement
HLF bid round 1 prep
HLF bid round 1 - submission
project review
executive report on review
HLF bid round 1 - decision
complete / agree permisison to start docs
HLF round 2 bid preparation
Design team appt
inception mtg / feasibility review
RIBA stage 2 design
stage 2 gateway review
RIBA stage 3 design
executive project approvals
HLF round 2 bid submission
Planning / LBC apps
HLF round 2 bid decision
Public Consultation / Engagement
advertise project development officer post
appoint project development officer
Activity Planning
Additional archaeology
detailled briefs for delivery stage
Permission to start
DELIVERY PHASE
detail design work
construction contractr procurement
enabling works package
Contract award
18 mth construction programme
